CONFIDENTIAL

Development Driller II - Stack on Stack option

ID		Task Name	Duration	Start	Finish
1		**Sub Sea Engineering tasks**	7 days	Wed 5/12/10	Tue 5/18/10
2		locate 5 - 4 k regulators and ship to DD II, clear installation w Hydril	3 days	Sat 5/15/10	Mon 5/17/10
3		Riser Analysis - SES	3 days	Wed 5/12/10	Fri 5/14/10
4		Analysis of Riser integrity - Aker - incl Eng Review	1 day	Sat 5/15/10	Sat 5/15/10
5		Machining and prep of 1 jnt with 2 x 4" ball valves incl 90 deg bends	2 days	Sun 5/16/10	Mon 5/17/10
6		Machining of 2 jnts - perforated w 12 x 8" holes	1 day	Sun 5/16/10	Sun 5/16/10
7	✓	Preping and welding 2 riser isolation plugs	1 day	Sat 5/15/10	Sat 5/15/10
8	✓	Testing & repair of HC connector @ CIW	2 days	Fri 5/14/10	Sat 5/15/10
9	✓	locate test stump - HC connector - DD II	1 day	Sat 5/15/10	Sat 5/15/10
10	✓	function test HC	2 days	Fri 5/14/10	Sat 5/15/10
11		locate bolts and seal kit on DEN to ship to DD II	1 day?	Sun 5/16/10	Sun 5/16/10
12		review actions resulting from PEER review	4 days	Fri 5/14/10	Mon 5/17/10
13		prepare Datum drawings with HC Connector	1 day	Mon 5/17/10	Mon 5/17/10

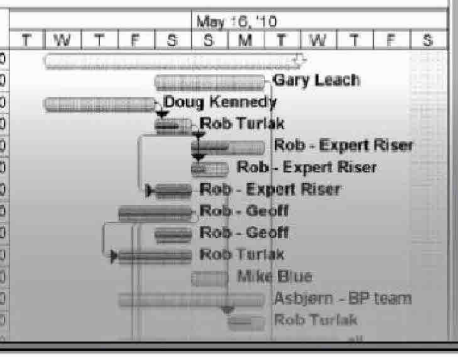

Development Driller II - Stack on Stack option
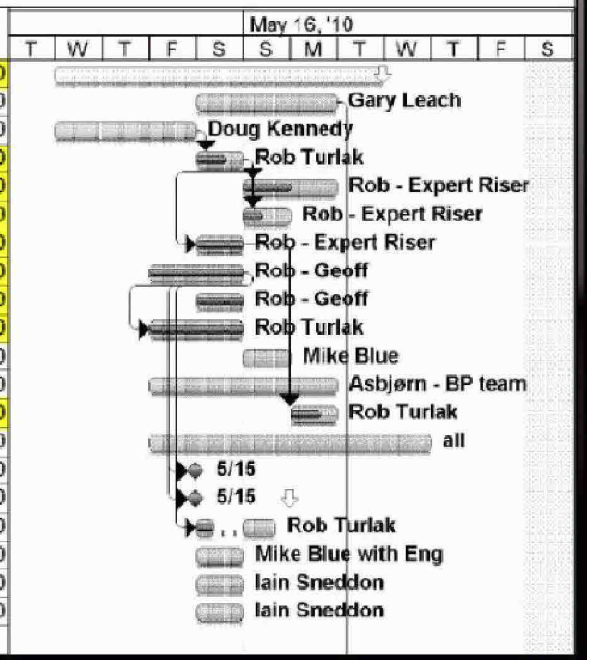
ID		Task Name	Duration	Start	Finish
1		**Sub Sea Engineering tasks**	7 days	Wed 5/12/10	Tue 5/18/10
2		locate 5 - 4 k regulators and ship to DD II, clear installation w Hydril	3 days	Sat 5/15/10	Mon 5/17/10
3		Riser Analysis - SES	3 days	Wed 5/12/10	Fri 5/14/10
4		Analysis of Riser integrity - Aker - incl Eng Review	1 day	Sat 5/15/10	Sat 5/15/10
5		Machining and prep of 1 jnt with 2 x 4" ball valves incl 90 deg bends	2 days	Sun 5/16/10	Mon 5/17/10
6		Machining of 2 jnts - perforated w 12 x 8" holes	1 day	Sun 5/16/10	Sun 5/16/10
7	✓	Preping and welding 2 riser isolation plugs	1 day	Sat 5/15/10	Sat 5/15/10
8	✓	Testing & repair of HC connector @ CIW	2 days	Fri 5/14/10	Sat 5/15/10
9	✓	locate test stump - HC connector - DD II	1 day	Sat 5/15/10	Sat 5/15/10
10	✓	function test HC	2 days	Fri 5/14/10	Sat 5/15/10
11		locate bolts and seal kit on DEN to ship to DD II	1 day?	Sun 5/16/10	Sun 5/16/10
12		review actions resulting from PEER review	4 days	Fri 5/14/10	Mon 5/17/10
13		prepare Datum drawings with HC Connector	1 day	Mon 5/17/10	Mon 5/17/10
14		prepare documentation package for riser analysis, modification, eqt	6 days?	Fri 5/14/10	Wed 5/19/10
15	✓	decision on the Well Head Gasket retention system	1 day	Sat 5/15/10	Sat 5/15/10
16	✓	methanol in connector - CIW check	1 day	Sat 5/15/10	Sat 5/15/10
17		guiding - bottom end of HC connector	1 day	Sat 5/15/10	Sun 5/16/10
18		DP system analysis - for DD II (Richard Simpson - BP)	1 day	Sat 5/15/10	Sat 5/15/10
19		prepare and submit all relevant procedures for rig review via Mike B.	1 day	Sat 5/15/10	Sat 5/15/10
20		review Anchor Winch 7 - operating system and documentation	1 day	Sat 5/15/10	Sat 5/15/10
21
