BP

11261N.2

Draft for Review 29-May 0900 - Rev C

Containment / BOP on BOP Level 1
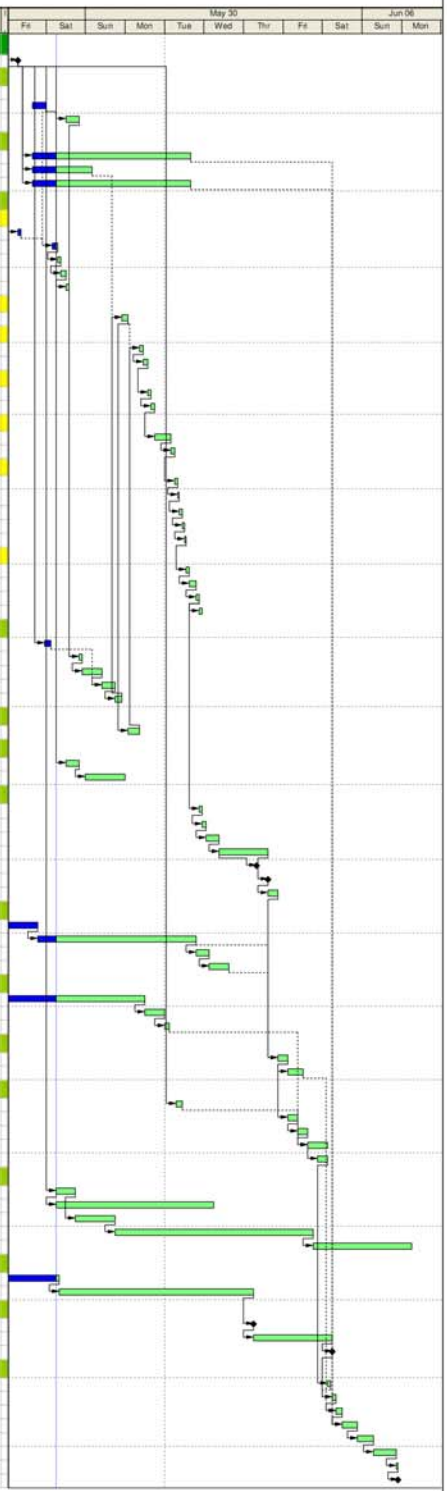
Activity ID	Activity Name	inin	Start	Finish	Vessel
	Containment Plan	216	26-May-10 19:00 A	07-Jun-10 06:00	
A1400	Commence Offshore Ops for Containment	0	26-May-10 07:00 A		
	Top Kill Pumping Operation - B Kelly	8	26-May-10 13:00 A	29-May-10 20:00	
A1000	Top Kill Begin Pumping Operations - Daylight Hours	0	26-May-10 13:00 A		
A1010	Stop Operations to Allow Pumping Activities - May 28th	0	28-May-10 16:00 A	29-May-10 00:00 A	
A1060	Stop Operations to Allow Pumping Activities - May 29th Yes/No	8	29-May-10 12:00	29-May-10 20:00	
	Procedures	82	28-May-10 16:00 A	01-Jun-10 16:00	
A1450	Manifold & Jumper Installation Procedure	82	28-May-10 16:00 A	01-Jun-10 16:00	
A1480	Contingency Cutting 45' from BOP & Top of Riser Procedure	22	28-May-10 16:00 A	30-May-10 04:00	
A1620	Manifold & Jumper Commissioning Procedure	82	28-May-10 16:00 A	01-Jun-10 16:00	
	Cut & Remove Horizon Riser	89	28-May-10 07:00 A	01-Jun-10 23:00	
	Under Flange Work - S Bond	8	28-May-10 07:00 A	29-May-10 14:00	
A1090	Under Flange Work - Place Plugs in Flange Alignment Holes	0	28-May-10 07:00 A	28-May-10 09:00 A	
A1140	Under Flange Work - Choke Line Coflex Removal	1	29-May-10 04:00 A	29-May-10 07:00	OB
A1150	Under Flange Work - Choke Hub Plug	2	29-May-10 07:00	29-May-10 09:00	OB
A1220	Under Flange Work - Kill Line Coflex Removal	3	29-May-10 09:00	29-May-10 12:00	OB
A1230	Under Flange Work - Kill Hub Plug	2	29-May-10 12:00	29-May-10 14:00	OB
	Mobilize to Make Cuts - A. Ginnard	4	30-May-10 22:00	31-May-10 02:00	
A1050	Mobilize to make cuts	4	30-May-10 22:00	31-May-10 02:00	Poseidon
	Diamond Wire Tool Test - A. Ginnard	5	31-May-10 09:00	31-May-10 14:00	
A1080	Diamond Wire - Deploy Crane with Rigging to Depth	2	31-May-10 09:00	31-May-10 11:00	Poseidon
A1490	Diamond Wire - Test Fit to Riser	3	31-May-10 11:00	31-May-10 14:00	Poseidon
	Reconfigure Riser Rigging - A. Ginnard	4	31-May-10 14:00	31-May-10 18:00	
A1500	Adjust Rigging	2	31-May-10 14:00	31-May-10 16:00	Poseidon
A1510	Rig Winch Line to Riser pipe	2	31-May-10 16:00	31-May-10 18:00	Poseidon
	Cut Choke & Kill Lines - A. Ginnard	12	31-May-10 18:00	01-Jun-10 06:00	
A1520	Super Grinder - Remove 4 External Lines	10	31-May-10 18:00	01-Jun-10 04:00	Poseidon
A1530	Super Grinder - Remove External Bracket	2	01-Jun-10 04:00	01-Jun-10 06:00	Poseidon
	Cut 1 (Shear) - A. Ginnard	7	01-Jun-10 06:00	01-Jun-10 13:00	
A1540	Lower Shear to Depth	2	01-Jun-10 06:00	01-Jun-10 08:00	Poseidon
A1560	Hook up Hydraulics	1	01-Jun-10 08:00	01-Jun-10 09:00	Poseidon
A1550	Position Shear on Pipe	2	01-Jun-10 09:00	01-Jun-10 11:00	Poseidon
A1570	Make Cut	1	01-Jun-10 11:00	01-Jun-10 12:00	Poseidon
A1580	Release Shear	1	01-Jun-10 12:00	01-Jun-10 13:00	Poseidon
	Cut 2 (Diamond Wire) - A. Ginnard	10	01-Jun-10 13:00	01-Jun-10 23:00	
A1600	Position and Latch Diamond Wire Saw	2	01-Jun-10 13:00	01-Jun-10 15:00	Poseidon
A1590	Make Diamond Wire Cut	4	01-Jun-10 15:00	01-Jun-10 19:00	Poseidon
A1610	Wet Store Riser	2	01-Jun-10 19:00	01-Jun-10 21:00	Poseidon
A1640	Recover Basket	2	01-Jun-10 21:00	01-Jun-10 23:00	Poseidon
	Removal of Top Kill Equipment from Riser - B Kelly	26	28-May-10 23:00 A	30-May-10 22:00	
A1390	Install Mudmats for 150' Jumpers	0	28-May-10 23:00 A	29-May-10 03:00 A	
A1190	Secure Choke & Kill Vlvs via the Q4000 through Yellow Pod	2	29-May-10 20:00	29-May-10 22:00	Q4000
A1210	450' Coflon Disconnect	12	29-May-10 22:00	30-May-10 10:00	BOA Deep C
A1200	Disconnect 150' 2x at LMRP & Hang off on BOP/ Wet Park	8	30-May-10 10:00	30-May-10 18:00	BOA Deep C
A1240	Install Caps on Choke & Kill Hubs	4	30-May-10 18:00	30-May-10 22:00	
	Install Rigging Slings to LMRP - A. Ginnard	7	31-May-10 02:00	31-May-10 09:00	
A1040	Install Rigging Slings to LMRP	7	31-May-10 02:00	31-May-10 09:00	Poseidon ?
	Subsea Dispersant - M. Lewis/K. Li / J Hughes	36	29-May-10 12:00	31-May-10 00:00	
A1460	Installation of 800ft Hose to BOP	8	29-May-10 12:00	29-May-10 20:00	
A1470	Ready for Subsea dispersant injection	24	30-May-10 00:00	31-May-10 00:00	Sk. Neptune
	Containment with Top Cap Over LMRP - D Stolz / D Schilling	48	01-Jun-10 21:00	03-Jun-10 21:00	
A1030	Assess Diamond Cut for preferred Top Cap	2	01-Jun-10 21:00	01-Jun-10 23:00	Enterprise
A1020	Engage \ J Lock Top Cap	2	01-Jun-10 23:00	02-Jun-10 01:00	Enterprise
A1100	Move & Land Top Cap over LMRP	8	02-Jun-10 01:00	02-Jun-10 09:00	Enterprise
A1110	Prepare for Flow Back utilizing Top Cap (Production Time)	30	02-Jun-10 09:00	03-Jun-10 15:00	Enterprise
A1440	Monitor requirement for offloading to Barge Massachusetts	0	03-Jun-10 08:00		Enterprise
A1120	Stop Production	0		03-Jun-10 15:00	Enterprise
A1370	Enterprise - Move off Station	6	03-Jun-10 15:00	03-Jun-10 21:00	Enterprise
	Manufacture of Manifold Vent Assembly - S Bond	105	27-May-10 01:00 A	02-Jun-10 15:00	
A1320	Finalize Design of Manifold Vent Assembly	0	27-May-10 01:00 A	26-May-10 19:00 A	N/A
A1330	Manufacture Manifold Vent Assembly	85	26-May-10 19:00 A	01-Jun-10 19:00	N/A
A1360	Transport Manifold Vent Assembly Houston to Fourchon	8	01-Jun-10 19:00	02-Jun-10 03:00	N/A
A1380	Transport Manifold Vent Assembly Fourchon to BOA Deep C	12	02-Jun-10 03:00	02-Jun-10 15:00	
	Manufacture of BOP Top Hat Contingency - S Bond	69	27-May-10 13:00 A	01-Jun-10 03:00	
A1410	Manufacture BOP Top Hat	54	27-May-10 13:00 A	31-May-10 12:00	N/A
A1420	Transport BOP Top Hat	12	31-May-10 12:00	01-Jun-10 00:00	
A1430	Install on Mudmat	3	01-Jun-10 00:00	01-Jun-10 03:00	
	Install Manifold Vent Assembly - S Bond	15	03-Jun-10 21:00	04-Jun-10 12:00	
A1130	Install Manifold Vent Assembly	6	03-Jun-10 21:00	04-Jun-10 03:00	BOA Deep C
A1630	Hookup / Install Manifold End of Jumper	9	04-Jun-10 03:00	04-Jun-10 12:00	TBD
	LMRP Removal - J Wellings / R Simpson	92	01-Jun-10 07:00	05-Jun-10 03:00	
0430	Install Insert into LMRP Basket (prior to LRMP lift)	4	01-Jun-10 07:00	01-Jun-10 11:00	Vessel Opp
0420	Move Boa Deep C over Well Center & Hook-up to Pre-Installed Slings	6	04-Jun-10 03:00	04-Jun-10 09:00	BOA Deep C
0290	Open Connector via Yellow POD - Q4000	6	04-Jun-10 09:00	04-Jun-10 15:00	Q4000
0350	Lift LMRP / Laydown LMRP to Basket- Boa Deep C	12	04-Jun-10 15:00	05-Jun-10 03:00	BOA Deep C
0360	Cut and Remove Drill Pipe Stub - Poseidon	6	04-Jun-10 21:00	05-Jun-10 03:00	Poseidon
	Schlumberger DST Equipment Mobilization	216	29-May-10 06:00	07-Jun-10 06:00	
A1650	Completion of Pre-mobilization Testing / Equipment Build Out	12	29-May-10 06:00	29-May-10 18:00	N/A
A1690	Mobilization of DST Crews	96	29-May-10 06:00	02-Jun-10 06:00	N/A
A1660	Mobilization of Equipment from Fouchon to the Rig	24	29-May-10 18:00	30-May-10 18:00	N/A
A1670	Staging / Rigging Up Equipment on the Rig	120	30-May-10 18:00	04-Jun-10 18:00	N/A
A1680	Pressure Testing	60	04-Jun-10 18:00	07-Jun-10 06:00	N/A
	DDII BOP work prior to Splash - G Kidd / J Wellings	120	24-May-10 18:00 A	03-Jun-10 06:00	
A1340	DDII Stump Test	2	24-May-10 18:00 A	29-May-10 08:00	N/A
A1350	Modifications to BOP / Final Integration & Testing with Guide Frame	118	29-May-10 08:00	03-Jun-10 06:00	N/A
	Riser Deployment DDII BOP Stack - G Kidd / J Wellings	48	03-Jun-10 06:00	05-Jun-10 06:00	
A1170	Modified DDII BOP Ready to Splash	0		03-Jun-10 06:00	DDII
A1180	DDII Running BOP	48	03-Jun-10 06:00	05-Jun-10 06:00	DDII
A1160	DDII BOP at Depth	0	05-Jun-10 06:00		DDII
	Install DDII BOP to Horizon BOP Stack - G Kidd / J Wellings /...	43	05-Jun-10 03:00	06-Jun-10 22:00	
0300	Remove AX Ring (if present)	2	05-Jun-10 03:00	05-Jun-10 05:00	DDII
0260	Final Transit to Well Location	2	05-Jun-10 06:00	05-Jun-10 08:00	DDII
0370	Land BOP Stack on Horizon BOP	4	05-Jun-10 08:00	05-Jun-10 12:00	DDII
0380	Install Jumper Hose to DDII BOP	9	05-Jun-10 12:00	05-Jun-10 21:00	DDII
0440	Pump Glycol & Commission Manifold Hose	10	05-Jun-10 21:00	06-Jun-10 07:00	TBD
0410	System Test / Commissioning	14	06-Jun-10 07:00	06-Jun-10 21:00	DDII
0390	Open Choke / Close Rams / Close Choke	1	06-Jun-10 21:00	06-Jun-10 22:00	DDII
0400	Vent Shut-in Wellhead Pressure as Required	0		06-Jun-10 22:00	DDII
