



Development Driller II - Stack on Stack option

ID	Task Name	Duration	Start	Finish	May '10															
					T	W	T	F	S	S	M	T	W	T	F	S				
1	Sub Sea Engineering tasks	7 days	Wed 5/12/10	Tue 5/18/10																
2	locate 5 - 4 k regulators and ship to DD II, clear installation w Hydril	3 days	Sat 5/15/10	Mon 5/17/10																
3	Riser Analysis - SES	3 days	Wed 5/12/10	Fri 5/14/10																
4	Analysis of Riser integrity - Aker - incl Eng Review	1 day	Sat 5/15/10	Sat 5/15/10																
5	Machining and prep of 1 jnt with 2 x 4" ball valves incl 90 deg bends	2 days	Sun 5/16/10	Mon 5/17/10																
6	Machining of 2 jnts - perforated w 12 x 8" holes	1 day	Sun 5/16/10	Sun 5/16/10																
7	Preping and welding 2 riser isolation plugs	1 day	Sat 5/15/10	Sat 5/15/10																
8	Testing & repair of HC connector @ CIW	2 days	Fri 5/14/10	Sat 5/15/10																
9	locate test stump - HC connector - DD II	1 day	Sat 5/15/10	Sat 5/15/10																
10	function test HC	2 days	Fri 5/14/10	Sat 5/15/10																
11	locate bolts and seal kit on DEN to ship to DD II	1 day?	Sun 5/16/10	Sun 5/16/10																
12	review actions resulting from PEER review	4 days	Fri 5/14/10	Mon 5/17/10																
13	prepare Datum drawings with HC Connector	1 day	Mon 5/17/10	Mon 5/17/10																

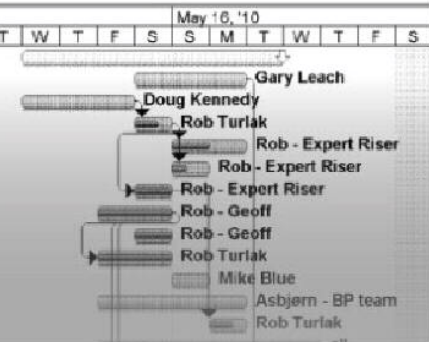

Development Driller II - Stack on Stack option

ID	Task Name	Duration	Start	Finish	May '10															
					T	W	T	F	S	S	M	T	W	T	F	S				
1	Sub Sea Engineering tasks	7 days	Wed 5/12/10	Tue 5/18/10																
2	locate 5 - 4 k regulators and ship to DD II, clear installation w Hydril	3 days	Sat 5/15/10	Mon 5/17/10																
3	Riser Analysis - SES	3 days	Wed 5/12/10	Fri 5/14/10																
4	Analysis of Riser integrity - Aker - incl Eng Review	1 day	Sat 5/15/10	Sat 5/15/10																
5	Machining and prep of 1 jnt with 2 x 4" ball valves incl 90 deg bends	2 days	Sun 5/16/10	Mon 5/17/10																
6	Machining of 2 jnts - perforated w 12 x 8" holes	1 day	Sun 5/16/10	Sun 5/16/10																
7	Preping and welding 2 riser isolation plugs	1 day	Sat 5/15/10	Sat 5/15/10																
8	Testing & repair of HC connector @ CIW	2 days	Fri 5/14/10	Sat 5/15/10																
9	locate test stump - HC connector - DD II	1 day	Sat 5/15/10	Sat 5/15/10																
10	function test HC	2 days	Fri 5/14/10	Sat 5/15/10																
11	locate bolts and seal kit on DEN to ship to DD II	1 day?	Sun 5/16/10	Sun 5/16/10																
12	review actions resulting from PEER review	4 days	Fri 5/14/10	Mon 5/17/10																
13	prepare Datum drawings with HC Connector	1 day	Mon 5/17/10	Mon 5/17/10																
14	prepare documentation package for riser analysis, modification, eqt	6 days?	Fri 5/14/10	Wed 5/19/10																
15	decision on the Well Head Gasket retention system	1 day	Sat 5/15/10	Sat 5/15/10																
16	methanol in connector - CIW check	1 day	Sat 5/15/10	Sat 5/15/10																
17	guiding - bottom end of HC connector	1 day	Sat 5/15/10	Sun 5/16/10																
18	DP system analysis - for DD II (Richard Simpson - BP)	1 day	Sat 5/15/10	Sat 5/15/10																
19	prepare and submit all relevant procedures for rig review via Mike B.	1 day	Sat 5/15/10	Sat 5/15/10																
20	review Anchor Winch 7 - operating system and documentation	1 day	Sat 5/15/10	Sat 5/15/10																
21																				

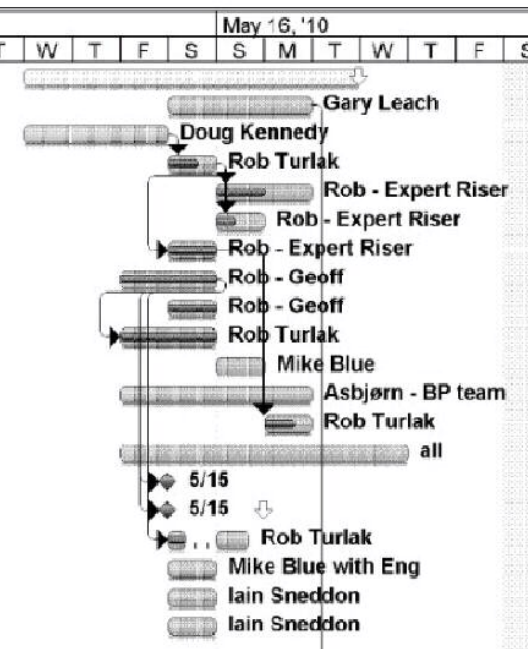

02
2590
53.0002
